


Request form – Stop logs

Customer: _____ Address: _____


Project: _____

1. Dimensions

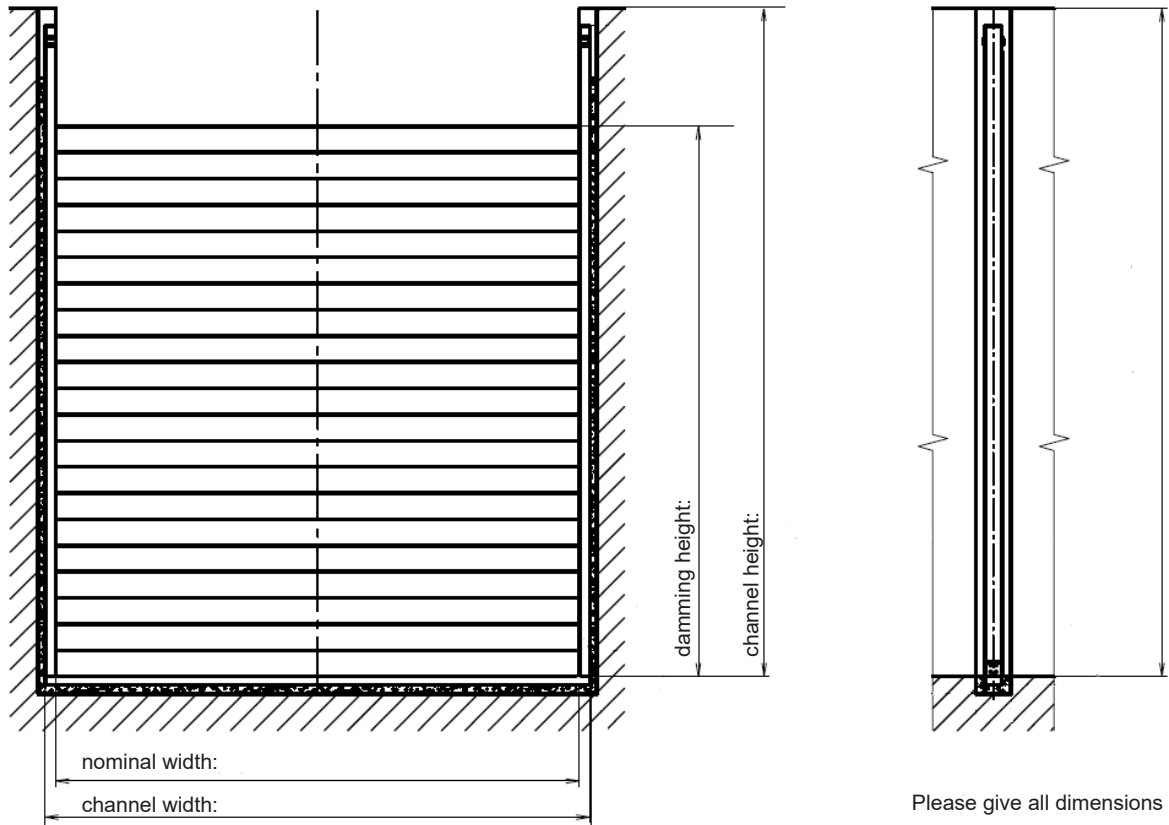


2. Installation



Frame doweled in front of the wall

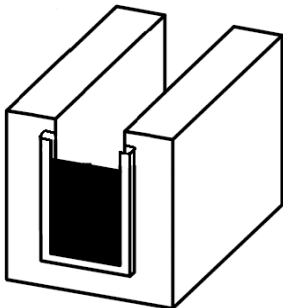

Frame embedding into channel groove

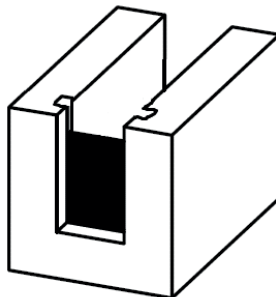

Frame doweled in the channel

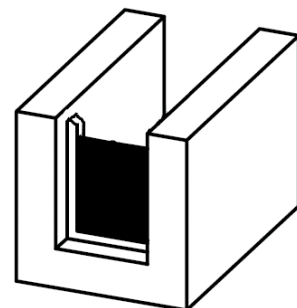



3. Materials

Stop logs:

- Stainless steel 1.4301
- Stainless steel 1.4404
- Aluminium
- Other : _____

Frame:

- Stainless steel 1.4301
- Stainless steel 1.4404
- Other: _____
- Steel 1.0038 hot-dip galvanized
- Steel 1.0038 epoxy coated


Sealing:

- EPDM
- NBR
- Other: _____

4. Lifting device

- Manual:
For a manually lifting of the logs

- Semiautomatic:
For lifting the logs with help of a crane e.g.



Remarks:

Telephone/E-Mail (for inquiry calls):
